


Trane Performance Climate Changer Air Handler

Unit Overview - AHU 1-1									
Amplication	Unit Size		External Dimensions	Weight					
Application	Unit Size	Height	Width	Length	Installed	Rigging			
Indoor unit	CSAA014	45.0 in	72.0 in	107.613 in	1978 lb	1864 lb			
Overtity of Chi	Quantity of Shipping Sections		Largest Ship Split			Flavetian			
Quantity of Shi			Width	Length	Heaviest Ship Split	Elevation			
2 piece(s)		86.5 in	72.0 in	74.4 in	1607 lb	0.00 ft			

Supply Fan							
Airflow	6500 cfm	Total Static Pressure	4.307 in H2O				

Construction Features						
Panel	2in. foam injected R-13 with thermal break					
	All unit inner panels - galvanized					
Integral Base Frame	6in. integral base frame					
Short Circuit Current Rating	65 kA					
Agency Approval	UL listed unit					

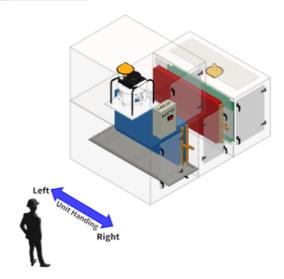

Unit Electrical				
Circuit	Voltage/Phase/Frequency	FLA	MCA	Max Fuse Size
Circuit number 1 Supply fan motor(s)	200-208/3/60	20.79 A	25.67	45.00

Unit Acoustics								
Sound Path	63 (Hz)	125	250	500	1K	2K	4K	8K
Supply top:	75 dB	82 dB	85 dB	84 dB	85 dB	82 dB	80 dB	77 dB
Return:	72 dB	74 dB	85 dB	72 dB	70 dB	70 dB	66 dB	63 dB
Casing:	74 dB	79 dB	86 dB	72 dB	75 dB	59 dB	60 dB	56 dB

Unit Controls		
	Controller Type	No controller
Warranty		

Warranty section Std. warranty only



Air mixing section - Position: 1										
Openings										
Face	Path	Туре	Airflow	Face Velocity	Area	Pressure Drop		Hood		
Тор	Retur	Sizeable rn rectangular opening	6500 cfm	767 ft/min	8.47 sq ft	0.00	0 in H2O	N/A		
			Fil	lter						
Туре		Frame	MERV	MERV Rating		Quantity		Size		
Pleated media -	MERV 13	2"	MER	RV 13	4.00 2.00			Sin.x20in. Sin.x25in.		
Pressure D	rop	Condition	Face V	elocity	ocity Airflow		Area			
0.683	0.683 Mid-life 450 ft/min		ft/min	6500 cfm		14	4.44 sq ft			
Section Options										
Door Location Right										

Heating coil section - Position: 2							
Coil Con	struction	Coil Performance					
Model	Hot water - 5/8" Shipping Coil, General (5W)	Сара	acity				
Rows	` '	Total	144.09 MBh				
	5/8in. tube diameter (15.875 mm)	A	ir				
Coil Connection		Flow	6500 cfm				
Tube Matl/Wall Thickness	.020" (0.508 mm) copper tubes	Entering Dry Bulb	34.00 F				
Fin Spacing	80 Per Foot	Leaving Dry Bulb	54.44 F				
Fin Material	Aluminum fins	Pressure Drop	0.082 in H2O				
Fin Type	Prima flo E (energy efficient)	Face Velocity	520 ft/min				
Face Area	Face Area 12.50 sq ft		Fluid				
Coil (top/single) H x L	30 in. (762 mm) X 60" (1524 mm) finned length	Flow	14.44 gpm				
Casing	Stainless steel	Entering	140.00 F				
	CompleteCoat(TM) Epoxy E-coat		120.00 F				
	Not Included	Pressure Drop					
Rigging Weight	61.3 lb	Tube Velocity					
Installed Weight		Reynolds Number					
Coil Section	on Options		Water				
Drain Pan Size	•	_	0.00025 hr-sq ft-deg F/Btu				
		Volume	2.25 gal				
Door Location Right		AHRI 410 CI	lassification				
		AHRI 410 Classification	NOT Certified by AHRI				
		Data Generation Date					
		Trane Select Assist update number	2840				

Note: Coil is NOT certified by AHRI. Coil is within the scope of AHRI Standard 410.



Cooling coil section - Posit	ion: 3			
Coil Con	struction	Coil Performance		
Model	Chilled water - 1/2" Unit Optimized, General (UW)	Сара	acity	
Rows	,	Total	361.52 MBh	
	1/2in. tube diameter (12.7 mm)	Sensible	220.61 MBh	
Coil Connection	,	A	ir	
Tube Matl/Wall Thickness	.016" (0.406 mm) copper tubes	Flow	6500 cfm	
Fin Spacing	110 Per Foot	Entering Dry Bulb	82.71 F	
Fin Material	Aluminum fins	Entering Wet Bulb	69.74 F	
Fin Type	Delta flo H (Hi efficient)	Leaving Dry Bulb	52.00 F	
Face Area	13.65 sq ft	Leaving Wet Bulb	51.90 F	
Coil (top/single) H x L	32 in. (813 mm) X 61" (1549 mm)	Pressure Drop	1.320 in H2O	
	illilled leligill	Face Velocity	476 ft/min	
-	Stainless steel	Fluid		
_	CompleteCoat(TM) Epoxy E-coat	Flow	51.46 gpm	
	Not Included	Entering	61	
Rigging Weight		Leaving		
Installed Weight		Pressure Drop	9.17 ft fluid	
Coil Section	on Options	Tube Velocity	3.53 ft/s	
Extended Drain and Vent	Holes only	Reynolds Number	10156.98	
	Stainless steel	Туре	Water	
Drain Pan Size		Fouling Factor	0.00000 hr-sq ft-deg F/Btu	
Drain Connection	0	Volume	11.41 gal	
Minimum Trap Height (L)		AHRI 410 C	lassification	
H Trap Dimension		AHRI 410 Classification		
J Trap Dimension		Data Generation Date	•	
Door Location	Right	Trane Select Assist update	7710/2024	
			2840	

Note: Coil is NOT certified by AHRI. Coil is within the scope of AHRI Standard 410.

Supply fan section - Position: 4								
Fan	Data	Motor	· Data					
Wheel Diameter/Type/Class	19.7 impeller fan full width	Voltage	200-208/3					
Fan Quantity	1	Impeller Fan Control Voltage	9.4 V					
Discharge Location	Top front	Impeller Fan HP per fan	8.050 hp					
Motor Location	Right side drive	FEI	1.42					
Drive Service Factor	Direct drive	Wire to air static efficiency	66.25 %					
Fan K-factor	2610.00	Note: Certified airflow performance per AHRI 430						
Fan Perf	formance	Fan Section Options						
Airflow	6500 cfm	Door Location	Right					
Total Static Pressure	4.307 in H2O	Door Guard	Yes					
Operating Speed	2113 rpm							
Fan electrical power (FEP)	4.96 kW							
Max Total Static Pressure @ 10V	4.885 in H2O							
Motor Interf	ace Options							
Selection Type	Selection Type MICP with H-O-A							
Voltage	Voltage 200-208/3							
Mounting Location	Mounting Location External mounting							

	Fan Discharge Options									
Face	Туре	Airflow	Face Velocity	Area	Pressure Drop	Exhaust Hood	Damper Torque Requirement			
Top Face Feature	Sizeable rectangular opening	6500 cfm	1331 ft/min	4.88 sq ft	0.222 in H2O	N/A	N/A			

Note: Certified by the AHRI Central Station Air-Handling Unit (AHU) Certification Program, based on AHRI Standard 430/431. AHRI certified units are subject to rigorous and continuous testing, have performance ratings independently measured and are third party verified. Certified units may be found in the AHRI Directory at www.ahridirectory.org.






Supply fan Acoustics									
Sound Path	63 (Hz)	125	250	500	1K	2K	4K	8K	
Supply top:	75 dB	82 dB	85 dB	84 dB	85 dB	82 dB	80 dB	77 dB	
Return:	72 dB	74 dB	85 dB	72 dB	70 dB	70 dB	66 dB	63 dB	
Casing:	74 dB	79 dB	86 dB	72 dB	75 dB	59 dB	60 dB	56 dB	

Pressure Drop in (in w.g.)	
Supply fan	
Air mixing section	0.68
Coil section	0.08
Coil section	1.32
Fan section	0.22
Internal Static Pressure	2.31
External Static Pressure	2.00
Total Static Pressure	4.31



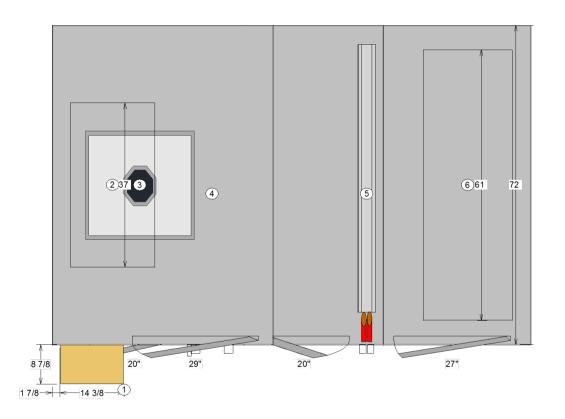

- 1 HMI Control box RH 21 x 14.38
- 2 Opening top 37 x 19
- 3 Plenum fan 19.7 impeller fan full width Supply fan Motorized impeller fan 200-208/3
- 4 Cooling coil 8 Rows Coil type 1/2" Unit Optimized, General (UW)
- 5 Heating coil 1 Rows Coil type 5/8" Shipping Coil, General (5W)
- 6 Opening top 61 x 20

Doors

20 width x 35 height 29 width x 35 height 27 width x 35 height

For maneuvering purposes, include 1.125 inches to each ship split length for overlapping panel flange. Flange will not add to overall installed unit length shown.


OPENING AND DIMENSIONS MAY VARY FROM CONTRACT DOCUMENTS / RETURN OF APPROVED DRAWINGS CONSTITUTES ACCEPTANCE OF THESE VARIANCES / NOT TO SCALE

Unit size: 14	Job Name: FSDB Kramer	Unit Casing: 2in Double Wall Foam
Product group: Indoor unit	6500 cfm	Proposal Number:
Integral base frame: 6in. integral base frame	Sales Office:	Tags: AHU 1-1
Paint:		1864.3 lb / 1978.5 lb



TRANE



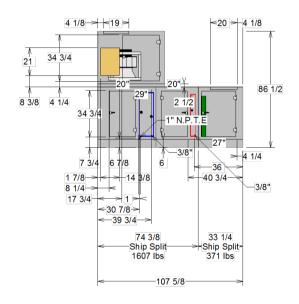

- 1 HMI Control box RH 21 x 14.38
- 2 Opening top 37 x 19
- 3 Plenum fan 19.7 impeller fan full width Supply fan Motorized impeller fan 200-208/3
- Cooling coil 8 Rows
 Coil type 1/2" Unit
 Optimized, General (UW)
- 5 Heating coil 1 Rows Coil type 5/8" Shipping Coil, General (5W)
- 6 Opening top 61 x 20
- 7 3/8"
- 8 1" N.P.T.E

Doors 20 width x 35 height 29 width x 35 height 27 width x 35 height

For maneuvering purposes, include 1.125 inches to each ship split length for overlapping panel flange. Flange will not add to overall installed unit length shown.


OPENING AND DIMENSIONS MAY VARY FROM CONTRACT DOCUMENTS / RETURN OF APPROVED DRAWINGS CONSTITUTES ACCEPTANCE OF THESE VARIANCES / NOT TO SCALE

Unit size: 14	Job Name: FSDB Kramer	Unit Casing: 2in Double Wall Foam	
Product group: Indoor unit	6500 cfm	Proposal Number:	
Integral base frame: 6in. integral base frame	Sales Office:	Tags: AHU 1-1	É
Paint:		1864.3 lb / 1978.5 lb	



TRANE° Performance





For maneuvering purposes, include 1.125 inches to each ship split length for overlapping panel flange. Flange will not add to overall installed unit length sh

Pos#	Module	Length	Weight
1	Air mixing section	33 1/4	371.22
2	Coil section	31 3/8	315.29
3	Coil section	43 1/8	757.54
4	Fan section	49 5/8	534.43
	Installed U	nit Weigh	t 1978.48 lbs




OPENING AND DIMENSIONS MAY VARY FROM CONTRACT DOCUMENTS / RETURN OF APPROVED DRAWINGS CONSTITUTES ACCEPTANCE OF THESE VARIANCES / NOT TO SCALE


Unit size: 14	Job Name: FSDB Kramer	Unit Casing: 2in Double Wall Foam	
Product group: Indoor unit	6500 cfm	Proposal Number:	
Integral base frame: 6in. integral base frame	Sales Office:	Tags: AHU 1-1	
Paint:		1864.3 lb / 1978.5 lb	



2024/07/10 09:37:27 Product Version: 1



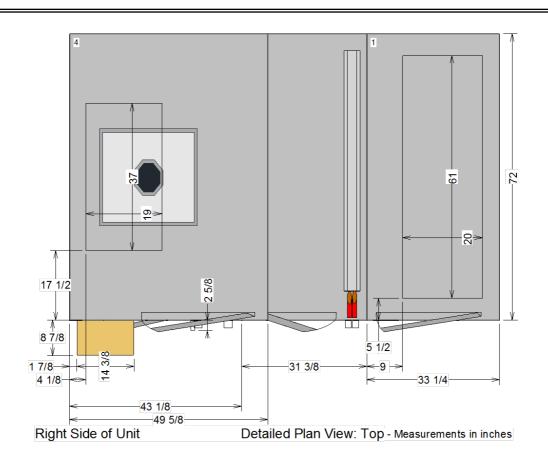

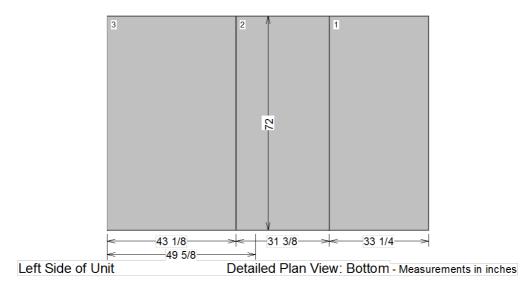

**Placement of electrical conduit may vary by a tolerance of 8" in any direction.


OPENING AND DIMENSIONS MAY VARY FROM CONTRACT DOCUMENTS / RETURN OF APPROVED DRAWINGS CONSTITUTES ACCEPTANCE OF THESE VARIANCES / NOT TO SCALE


Unit size: 14	Job Name: FSDB Kramer	Unit Casing: 2in Double Wall Foam	
		Proposal Number:	
Integral base frame: 6in. integral base frame	Sales Office:	Tags: AHU 1-1	
Paint:		1864.3 lb / 1978.5 lb	



2024/07/10 09:37:27 Product Version: 1



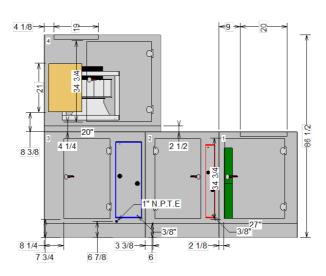



Detailed Elevation View: Left - Measurements in inches

OPENING AND DIMENSIONS MAY VARY FROM CONTRACT DOCUMENTS / RETURN OF APPROVED DRAWINGS CONSTITUTES ACCEPTANCE OF THESE VARIANCES / NOT TO SCALE


Unit size: 14	Job Name: FSDB Kramer	Unit Casing: 2in Double Wall Foam
Product group: Indoor unit	6500 cfm	Proposal Number:
Integral base frame: 6in. integral base frame	Sales Office:	Tags: AHU 1-1
Paint:		1864.3 lb / 1978.5 lb




Performance Climate Changer

Air Handlers





Detailed Elevation View: Front - Measurements in inches



Detailed Elevation View: Back - Measurements in inches

OPENING AND DIMENSIONS MAY VARY FROM CONTRACT DOCUMENTS / RETURN OF APPROVED DRAWINGS CONSTITUTES ACCEPTANCE OF THESE VARIANCES / NOT TO SCALE


Unit size: 14	Job Name: FSDB Kramer	Unit Casing: 2in Double Wall Foam	
Product group: Indoor unit	6500 cfm	Proposal Number:	
Integral base frame: 6in. integral base frame	Sales Office:	Tags: AHU 1-1	
Paint:		1864.3 lb / 1978.5 lb	



Performance Climate Changer

Air Handlers



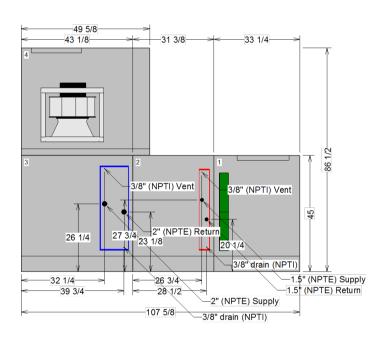


NPTI : National Pipe Thread Internal Connection NPTE : National Pipe Thread External Connection

OPENING AND DIMENSIONS MAY VARY FROM CONTRACT DOCUMENTS / RETURN OF APPROVED DRAWINGS CONSTITUTES ACCEPTANCE OF THESE VARIANCES / NOT TO SCALE

Unit size: 14	Job Name: FSDB Kramer	Unit Casing: 2in Double Wall Foam	
Product group: Indoor unit	6500 cfm	Proposal Number:	
Integral base frame: 6in. integral base frame	Sales Office:	Tags: AHU 1-1	
Paint:		1864.3 lb / 1978.5 lb	





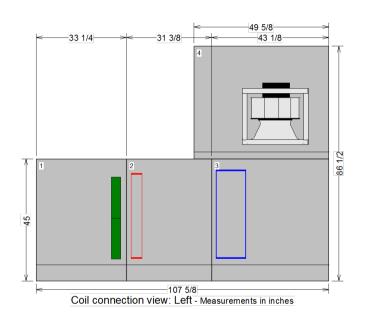


NPTI : National Pipe Thread Internal Connection NPTE : National Pipe Thread External Connection

OPENING AND DIMENSIONS MAY VARY FROM CONTRACT DOCUMENTS / RETURN OF APPROVED DRAWINGS CONSTITUTES ACCEPTANCE OF THESE VARIANCES / NOT TO SCALE

- 1				
١	Unit size: 14	Job Name: FSDB Kramer	Unit Casing: 2in Double Wall Foam	
١	Product group: Indoor unit	6500 cfm	Proposal Number:	
١	Integral base frame: 6in. integral base frame	Sales Office:	Tags: AHU 1-1	
١	Paint:		1864.3 lb / 1978.5 lb	





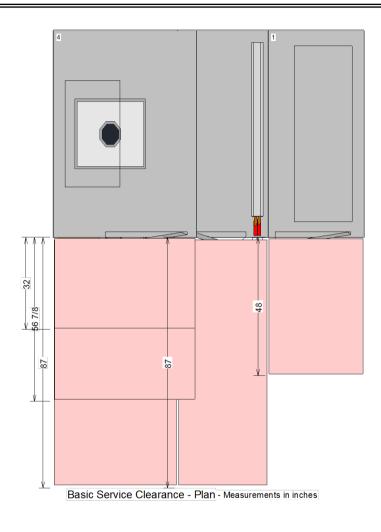


OPENING AND DIMENSIONS MAY VARY FROM CONTRACT DOCUMENTS / RETURN OF APPROVED DRAWINGS CONSTITUTES ACCEPTANCE OF THESE VARIANCES / NOT TO SCALE

Unit size: 14	Job Name: FSDB Kramer	Unit Casing: 2in Double Wall Foam	
Product group: Indoor unit	6500 cfm	Proposal Number:	4
Integral base frame: 6in. integral base frame	Sales Office:	Tags: AHU 1-1	Į
Paint:		1864.3 lb / 1978.5 lb	`





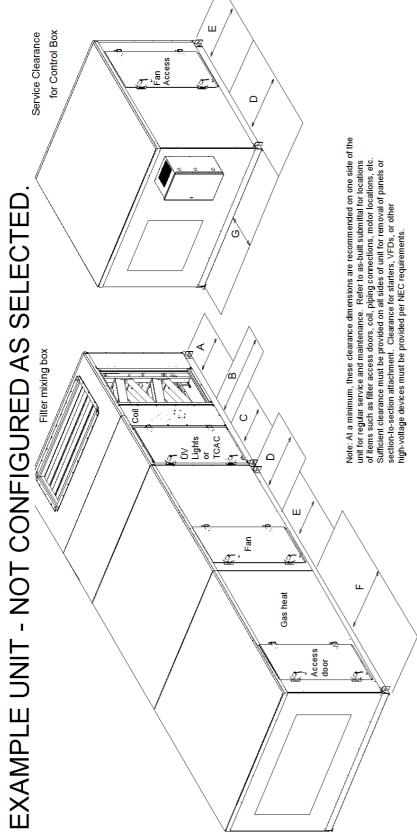


												f							
Component	က	4	9	œ	10	12	41	17	7	25	30	35	40	20	22	99	80	100	120
A (filter)	48	48	48	48	48	48	48	48	48	48	48	48	48	48	48	52	99	58	58
B (coil, humidifier)	48	59	59	99	22	82	87	87	95	95	109	115	128	141	141	156	156	170	197
B (staggered coil)	A/N	N/A	A/N	Ϋ́	A/N	₹ X	ĕ,	A/A	29	29	92	80	88	96	96	105	105	113	129
C (UV Lights)	48	48	48	48	48	48	48	48	48	48	48	48	48	48	48	52	56	58	58
C (TCAC)	43	59	59	63	75	25	83	83	58	58	83	22	83	83	83	83	83	75	83
D (External Starter, VFD, LV box or Overload box)	, 61	61	61	61	61	19	61	61	64	64	64	64	64	64	64	64	64	64	64
D (Internal Starter or VFD)	48	48	48	48	48	48	48	48	48	48	48	48	48	48	48	48	48	48	48
E (fan)	48	48	48	48	51	54	58	61	09	99	99	99	20	22	22	93	93	101	101
F (Gas Heat Ext Vestible)	N/A	N/A	89	06	108	100	100	105	115	115	118	136	140	156	156	170	179	180	N/A
F (Gas Heat Int Vestible)	N/A	N/A	56	63	74	62	84	84	92	95	106	112	125	138	138	153	153	167	194


Component	All Sizes
G (Side mount LV box)	36
G (Front mount LV box)	13




Base Detail

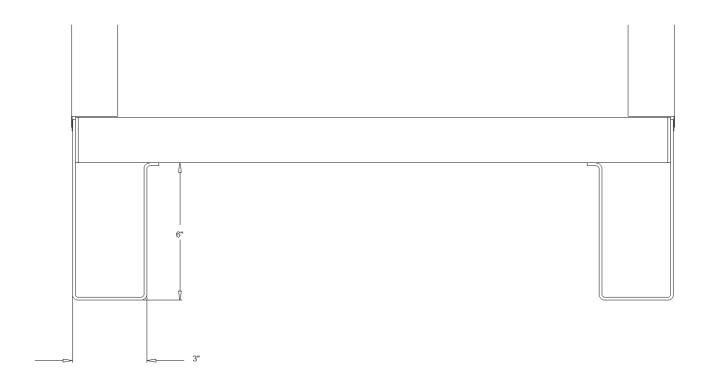



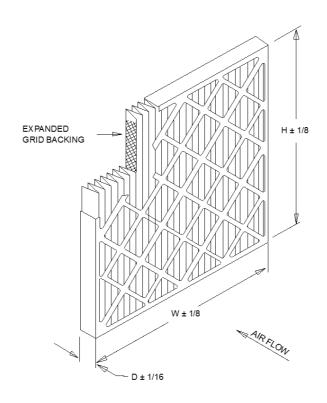

NOMINAL SIZE (WxHxD)	ACTUAL SIZE (WxHxD)	RATED AIR FLOW (CFM)	INITIAL RESISTANCE (IN. W.G.)	MEDIA AREA (SQUARE FEET)	FILTER UNIT WEIGHT (LBS)
12x24x2	11-3/8 x 23-3/8 x 1-3/4	1000	0.41	10.5	0.9
16x20x2	15-1/2 x 19-1/2 x 1-3/4	1120	0.41	10.9	1.1
16x25x2	15-1/2 x 24-1/2 x 1-3/4	1400	0.41	14.9	1.3
20x20x2	19-1/2 x 19-1/2 x 1-3/4	1400	0.41	14.5	1.3
20x24x2	19-3/8 x 23-3/8 x 1-3/4	1670	0.41	17.4	1.4
20x25x2	19-1/2 x 24-1/2 x 1-3/4	1750	0.41	18.5	1.4
24x24x2	23-3/8 x 23-3/8 x 1-3/4	2000	0.41	21.1	1.6

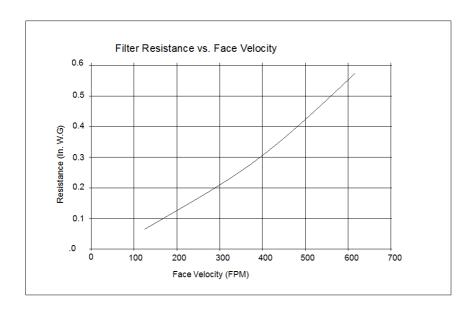


STANDARD CONSTRUCTION

- 1. 100 % Synthetic White Media
- 2. 17.5 Pleats Per Foot
- 3. Expanded Metal Pleat Supports
- 4. Moisture Resistant Beverage Board Frame
- 5. Double Wall Frame

NOTES

- 1. MERV 13 per ASHRAE 52.2-2012 Tested at 492 FPM on 24x24x2 Nominal Size
- 2. Final Resistance: 1.0" W.G.
- 3. Rated Velocity: 500 FPM
- 4. Classified per U.L. Standard 900 for Flammibility
- 5. Maximum Operating Temperature: 200 deg. F



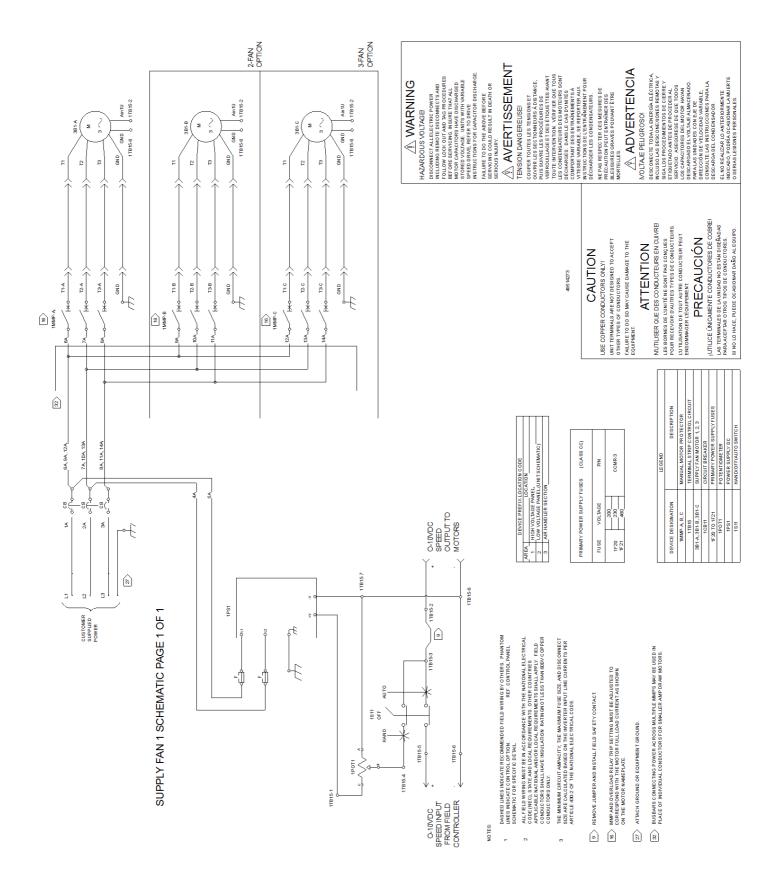

GENERAL

Per ASHRAE 62.1 recommendation, indoor air handling units will be wrapped to protect unit from intransit rain and debris.

Installing contractor is responsible for long term storage in accordance with the Installation, Operation, and Maintenance manual (CLCH-SVX07*-EN).

Unit shall be UL and C-UL Listed.

Supply fans within the scope of AHRI Standard 430 are "Certified by the AHRI Central Station Air-Handling Unit (AHU) Certification Program, based on AHRI Standard 430/431. AHRI certified units are subject to rigorous and continuous testing, have performance ratings independently measured and are third-party verified. Certified units may be found in the AHRI Directory at www.ahridirectory.org".

Unit sound performance data shall be reported as sound power. Trane, in providing this program and data, does not certify or warrant NC levels. These levels are affected by factors specific to each application and/or installation and therefore unable to be predicted or certified by Trane. Refer to product data for specific fan footnote references.

Refer to product data for AHRI certification status. Propylene glycol and calcium chloride, or mixtures thereof, are outside the scope of AHRI Standard 410 and, therefore, do not require AHRI rating or certification. For coils within the scope of AHRI Standard 410 cooling coil performance is certified in accordance with the AHRI Forced-Circulation Air-Cooling and Air-Heating Coils Certification Program which is based on AHRI Standard 410 within the Range of Standard Rating Conditions listed in Table 1 of the Standard. Certified units may be found in the AHRI Directory at www.ahridirectory.org. Heating performance for heat pump or condenser mode is not certified.

Unit Construction

All unit panels shall be 2" solid, double-wall construction to facilitate cleaning of unit interior. Unit panels shall be provided with a mid-span, no-through-metal, internal thermal break. Casing thermal performance shall be such that under 55°F supply air temperature and design conditions on the exterior of the unit of 81°F dry bulb and 73°F wet bulb, condensation shall not form on the casing exterior. Casing construction will comply with NFPA 90A.

All exterior and interior indoor AHU panels will be made of galvanized steel.

Unit Paint

Unit to ship unpainted from factory. If required, unit to be painted by 3rd party finisher, or by painting contractor at job site.

Casing Deflection

The casing shall not exceed 0.0042 inch deflection per inch of panel span at 1.00 times design static pressure. Maximum design static shall not exceed +8 inches w.g. in all positive pressure sections and -8 inches w.g. in all negative pressure sections.

Floor Construction

The unit floor shall be of sufficient strength to support a 300.0 lb load during maintenance activities and shall deflect no more than 0.0042 inch per inch of panel span.

Unit Base

Manufacturer to provide a full perimeter integral base frame for either ceiling suspension of units or to support and raise all sections of the unit for proper trapping. Indoor unit base frame will either be bolted construction or welded construction. All outdoor unit base frames shall be welded construction. For indoor units, refer to schedule for base height and construction type. Contractor will be responsible for providing a housekeeping pad when unit base frame is not of sufficient height to properly trap unit. Unit base frames not constructed of galvanized steel shall be chemically cleaned and coated with both a rust-inhibiting primer and finished coat of rust-inhibiting enamel. Unit base height to be included in total height required for proper trap height.

Insulation

Panel insulation shall provide a minimum thermal resistance (R) value of 13 ft²-h-ºF/Btu throughout the entire unit. Insulation shall completely fill the panel cavities in all directions so that no voids exist and settling of insulation is prevented.

Drain Pan

In sections provided with a drain pan, the drain pan shall be designed in accordance with ASHRAE 62.1. To address indoor air quality (IAQ) the drain pan shall be sloped in two planes promoting positive drainage to eliminate stagnant water conditions. Drain pan shall be insulated, and of double wall construction. The outlet shall be the lowest point on the pan, and shall be of sufficient diameter to preclude drain pan overflow under normally expected operating conditions. All drain pans connections shall have a threaded connection, extending a minimum of 2-1/2" beyond the unit base, and shall be made from the same material as the drain pan. Drain pan located under a cooling coil shall be of sufficient size to collect all condensate produced from the coil.

Refer to Product Data for specific information on which sections are supplied with a drain pan, the drain pan material and connection location.

Access Door Construction

Access doors shall be 2" double wall construction. Interior and exterior door panels shall be of the same construction as the interior and exterior wall panels respectively. All doors shall be provided with a thermal break construction of door panel and door frame. Gasketing shall be provided around the full perimeter of the doors to prevent air leakage. Surface mounted handles shall be provided to allow quick access to the interior of the functional section and to prevent through cabinet penetrations that could likely weaken the casing leakage and thermal performance. Handle hardware shall be designed to prevent unintended closure. Outswing doors shall have easily removable hinges and handles that can be relocated to change the door swing if needed. Door hinges shall be made of stainless steel.

All doors shall be a minimum of 60" high when sufficient height is available or the maximum height allowed by the unit height.

Door handles shall be provided for each latching point of the door necessary to maintain the specified air leakage integrity of the unit. An optional shatterproof window shall be provided in access doors where indicated on the plans. Window shall either be single pane, or thermal dual pane, as defined on schedule. Window shall be capable of withstanding unit operating pressures and shall be safe for viewing UV-C lamps.

Refer to Product Data for specific information on which sections are supplied with an access door, the door location, a single handle and a window.

Lifting Instructions

The air handling units must be rigged, lifted, and installed in strict accordance with the Installation, Operation, and Maintenance manual (CLCH-SVX07G-EN). The units are also to be installed in strict accordance with the specifications. Units may be shipped fully assembled or disassembled to the minimum functional section size in accordance with shipping and job site requirements.

Indoor units shall be shipped on an integral base frame (variable from the standard 2.5" to 8" height) for the purpose of mounting units to a housekeeping pad and providing additional height to properly trap condensate from the unit. The integral base frame may be used for ceiling suspension, external isolation, or as a housekeeping pad. Indoor sizes 3 to 30 will also be shipped with a shipping skid designed for forklift transport. Refer to the unit As-Built or Product Data section of the submittal for the base frame height of each unit.

All units will be shipped with an integral base frame designed with the necessary number of lift points for safe installation. All lifting lugs are to be utilized during lift. The lift points will be designed to accept standard rigging devices and be removable after installation.

MIXING SECTION

A mixing section shall be provided to support the damper assembly for outdoor, return, and/or exhaust air.

Title 24

The following specifications apply only to units with outside air and return air dampers, with actuators. The 5 year warranty applies only to these items.

This unit contains Economizer that meets or exceeds all mandatory requirements prescribed by Title 24, including but not limited to:

- 5 yr parts only warranty
- Successfully tested to 60,000 Actuations
- Less than 10 cfm/sq.ft. of damper leakage at 1" WG per AMCA 500L

Filters

Mixing sections shall be provided with a filter rack as indicated in the Product Data and As-Built sections of the submittal.

2 inch pleated media filters made with 100% synthetic fibers that are continuously laminated to a supported steel wire grid with water repellent adhesive shall be provided. Filters shall be capable of operating up to 625 fpm face velocity without loss of filter efficiency and holding capacity. The filters shall have a MERV 13 rating when tested in accordance with the ANSI/ASHRAE Standard 52.2.

COIL SECTION WITH FACTORY INSTALLED COIL

The coil section shall be provided complete with coil and coil holding frame. The coils shall be installed such that headers and return bends are enclosed by unit casings. If two or more cooling coils are stacked in the unit, an intermediate drain pan shall be installed between each coil and be of the same material as the primary drain pan. Like the primary drain pan, the intermediate drain pan shall be designed being of sufficient size to collect all condensation produced from the coil and sloped to promote positive drainage to eliminate stagnant water conditions. The intermediate pan shall begin at the leading face of the water-producing device and be of sufficient length extending downstream to prevent condensate from passing through the air stream of the lower coil. Intermediate drain pan shall include downspouts to direct condensate to the primary drain pan. The outlet shall be located at the lowest point of the pan and shall be sufficient diameter to preclude drain pan overflow under any normally expected operating condition.

Coil with Inspection

The coil section complete with a double-wall, shall include a removable door downstream of the coil for inspection, cleaning, and maintenance. Interior and exterior door panels shall be of the same construction as the interior and exterior wall panels, respectively. All doors shall be provided with a thermal break construction of door panel and door frame.

Casing penetrations supplied for hydronic drain and vents. Piping contractor shall provide extended piping.

No casing penetrations supplied for hydronic drain and vents. If required, piping contractor will need to drill drain and vent penetrations using factory located features provided in coil panel.

Water Coils (UP, WP, UW, UU, UA, 3W, 3U, W, 5W, 5A, WD, 5D, D1, D2, P, or TT)

The coils shall have aluminum fins and seamless copper tubes. Copper fins may be applied to coils with 5/8-inch tubes. Fins shall have collars drawn, belled, and firmly bonded to tubes by mechanical expansion of the tubes. The coil casing may be galvanized or stainless steel. Refer to the Product Data section of the submittal for the coil casing material.

The coils shall be proof-tested to 300 psig and leak-tested under water to 200 psig. Refer to the Product Data section of the submittals for AHRI certirification status.

Coil connections are constructed of cast iron with female connections, steel block with female connections or steel pipe with male connections. Type P or TT coil connections do not extend out of unit casing. All other water coil types have connections that extend out beyond unit casing. Headers on downstream coil bank of staggered coil sections do not extend beyond the unit casing and must be completed by the on-site piping contractor.

Tubes are 1/2" [13 mm] OD 0.016" [0.406 mm] thick copper.

Tubes are 5/8" [16 mm] OD 0.020" [0.508 mm] thick copper.

Coil Coating

Coil shall have a flexible epoxy polymer e-coat uniformly applied to all coil surface areas without material bridging between fins. Coating process shall ensure complete coil encapsulation and a uniform dry film thickness from 0.8 - 1.2 mil on all surface areas including fin edges. Superior hardness characteristics of 2H per ASTM D3363-92A and a cross-hatch adhesion of 4B-5B per ASTM B3359-93. Impact resistance shall be up to 160 in/lb per ASTM D2794-93. Humidity and water immersion resistance shall be up to a minimum 1000 and 260 hours respectively (ASTM D2247-92 and ASTM D870-02). Corrosion durability shall be confirmed through testing to no less than 5,000 hours salt spray per ASTM B117-90 using scribed aluminum test coupons.

MOTORIZED IMPELLER FAN SECTION

Direct plenum fans provided with electronically commutated external- rotor motor with integrated control electronics, radial aluminum impeller with backward curved, continuously welded blades.

- 1. Individual Fan Assemblies shall be statically and dynamically balanced in two planes as per DIN / ISO 1940 to balancing grade G 6.3.
- 2. Fan-to-fan interaction can cause a significant increase in individual fan vibration when mounted to the same structure. Fans applied in an array shall be tested as a system and the total fan vibration shall be less that 0.42 (in/s) RMS including all fan-to-fan interaction. This system effect shall be accounted for by the air handler manufacturer. Individual fan vibration performance values shall not be acceptable.
- 3. Fan performance is "Certified by the AHRI Central Station Air-Handling Unit (AHU) Certification Program, based on AHRI Standard 430/431. AHRI certified units are subject to rigorous and continuous testing, have performance ratings independently measured and are third-party verified. Certified units may be found in the AHRI Directory at www.ahridirectory.org". Fan shall be spaced to minimize aerodynamic fan interaction. Minimum center-to-center spacing between fans shall be 1.6 diameter ratio to ensure proper performance.
- 4. Fan wheels shall be constructed of materials that comply with UL 1995/60335 requirements of flame and smoke spread per NFPA 90A. The flame spread index not exceeding 25 and a smoke-developed index not exceeding 50.
- 5. Fan Electrical Power (FEP) rated in accordance with AHRI 430-2020.
- 6. Motor shall contain integrated PID controller and accept a 0-10VDC input signal for variable speed control.
- 7. Motor efficiency class shall comply with IE4
- 8. Fan system manufacturer must stock replacement parts in North America
- 9. Fan array shall be designed and constructed for easy field assembly and maintenance. Fan shall be assembled to bulkhead wall with minimal fasteners and the fan shall have quick disconnects for the high voltage and low voltage connections.
- 10. For units utilizing multiple fans in a fan section, a fan curve shall be provided showing the performance of the entire bank of fans at design conditions. In addition, a fan curve shall be provided showing the performance of each individual fan in the bank of fans at design conditions. Also a fan curve shall be provided showing the performance of the bank of fans, if one fan is down. The percent redundancy of the bank of fans with one fan down shall be noted on the fan curve or in the tabulated fan data.

On units supplied with plenum or motorized impeller fans, door guard(s) shall be supplied on the access door(s) to the fan and those downstream access door(s) where unintended access to the plenum or motorized impeller fan could occur. Door guard is intended to deter unauthorized entry and incidental contact with rotating components. Refer to the Product Data section for fans with access door guard(s).

Motorized Impeller Control Panel with Hand-Off-Auto Switch

The fan shall be provided with a factory installed NEMA 1 or NEMA 3R motorized impeller motor control panel. The control panel provides a common externally accessible disconnect means, motor over current protection for each fan and a terminal block for ease of control wiring. The box shall include:

- 1.Individual motor protection with individual disconnnecting means with lockable feature. Fusable motor protection is not permissable.
- 2. Fused main panel disconnect with lock out tag out capability
- 3.Common control terminal block for common signal wiring. Single 0-10vdc signal used for fan speed control.
- 4.Control panel box shall be UL508a compliant and manufactured by a UL508a approved manufacturer or UL certified during air handler installation.
- 5. Control panel to include hand/off/auto switch for unit startup and commissioning.
- 6. Dial potentiometer to be included to for manual speed control in the 'hand' position.
- 7.Control panel shall be able to operate fans without a BAS signal for purposes of troubleshooting and commissioning

_			
-2n	11	etai	IS
ıaıı	ப	יכומו	כיו

Unit Size	19FM	Operating RPM	2,113 rpm
Control Signal	9.4 V	Altitude	0.00 ft


Voltage

Operating Airflow6,500 cfmDesign Temp.52.00 FOperating Static4.307 in H2OEfficiency66.25 %Pressure

Design voltage is less than 10. Ensure the air delivery system can handle being pressurized to the Maximum static pressure detailed in the product data and shown on the fan curve.

19" 6KW 208-230V 1 Fan Motorized Impeller Array - Single Fan

19" 6KW 208-230V 1 Fan Motorized Impeller Array

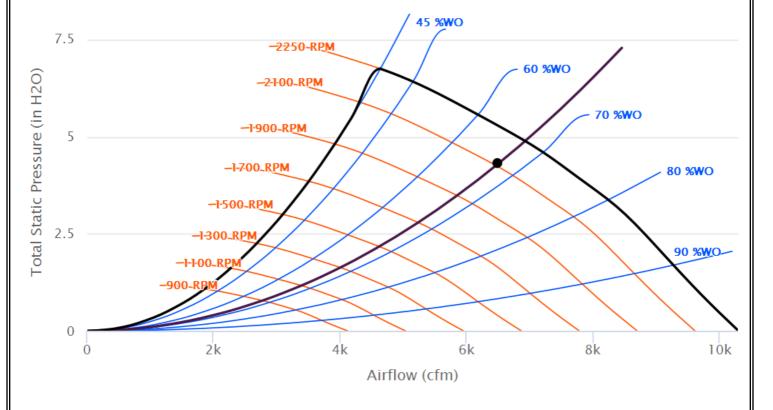

4 SUPPLY FAN (4)MICBINITIAL (5)MICBINITIAL (6)MICBINITIAL (6)MICBINITIAL (7)MICBINITIAL (6)MICBINITIAL (7)MICBINITIAL (7)MICBINITIAL (7)MICBINITIAL (8)MICBINITIAL (9)MICBINITIAL (10)MICBINITIAL (11)MICBINITIAL (12)MICBINITIAL (13)MICBINITIAL (14)MICBINITIAL (14)MICBINITIAL (15)MICBINITIAL (15)MICBINITIAL (16)MICBINITIAL (17)MICBINITIAL (17)MICBINIT

Trane

DATE 7/10/2024

SOFTWARE VERSION

DRAWING VERSION

Trane

CSIA—SCHEMATIC

UNIT SIZE: 14

UNIT TAG: AHU 1—1

LEGEND DETAIL 1

	BUILD						PWR	SIGNAL		POWER
POS#	GROUP	DESCRIF	PTION	l	PT	LABEL	HR-WIRE	HR-WIRE	XFMR	VA
4	3	Supply	Fan	Speed	AO1	VFD1				

PRAWN BY SERVICE ACCOUNT	Trane	
DATE 7/10/2024		CSIA-SCHEMATIC
SOFTWARE VERSION 1.4.0		UNIT SIZE: 14
DRAWING VERSION		UNIT TAG: AHU 1-1
